


ID	Task Name	Duration	Start	Finish	Predecessors	11/08	12/08	1/09	2/09	3/09	4/09	5/09	6/09	7/09	8/09	9/09	10/09	11/09	12/09	1/10	2/10	3/10	4/10	
1	Notice to Proceed/Mobilization	0 days	Mon 4/13/09	Mon 4/13/09		B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B
2	Submittals	50 days	Mon 4/13/09	Fri 6/19/09	1																			
3	Equipment Fabrication	80 days	Mon 6/22/09	Fri 10/9/09	2																			
4	Grading/Site Prep	20 days	Mon 6/22/09	Fri 7/17/09	2																			
5	Headworks	40 days	Mon 7/20/09	Fri 9/11/09	4																			
6	Influent Junction Box	10 days	Mon 9/14/09	Fri 9/25/09	5																			
7	Concrete Coatings	40 days	Mon 9/28/09	Fri 11/20/09	6																			
8	Concrete Foundation for Metal Building	10 days	Mon 9/28/09	Fri 10/9/09	6																			
9	Metal Building	10 days	Mon 10/12/09	Fri 10/23/09	8																			
10	Misc Metals Installation	15 days	Mon 10/26/09	Fri 11/13/09	9																			
11	Install Treatment Equipment	40 days	Mon 11/23/09	Fri 1/15/10	3,9,7																			
12	Yard Piping	20 days	Mon 12/21/09	Fri 1/15/10	11FF																			
13	Electrical	100 days	Mon 8/31/09	Fri 1/15/10	11FF																			
14	Paving/Regrading/Sitework Touchup	20 days	Mon 1/18/10	Fri 2/12/10	11,13																			
15	Startup	10 days	Mon 2/15/10	Fri 2/26/10	14																			
16	Substantial Completion	0 days	Fri 2/26/10	Fri 2/26/10	15																			
17	Punchlist	20 days	Mon 3/1/10	Fri 3/26/10	16																			
18	Final Completion	0 days	Fri 3/26/10	Fri 3/26/10	17																			

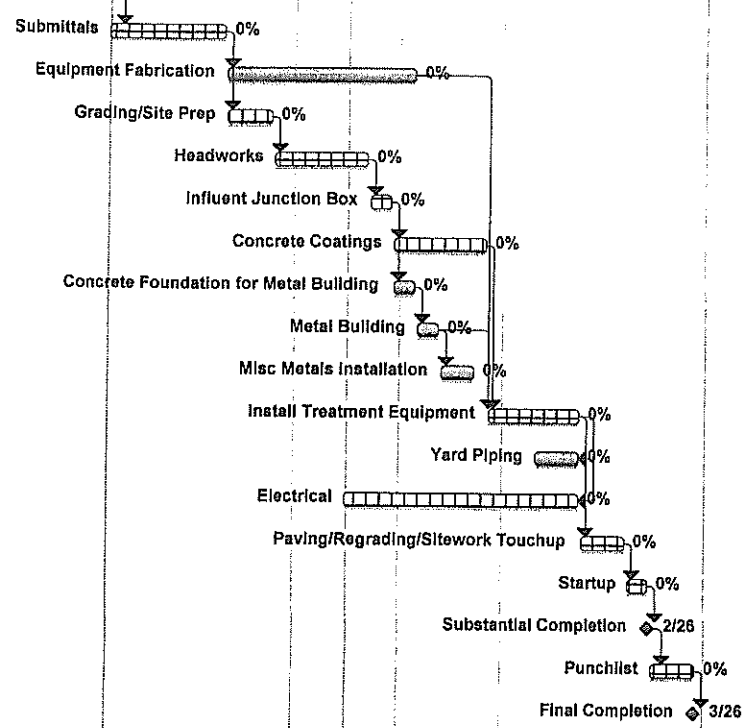

Project: Springtown Wastewater System Improvements
 Contractor: MELA Contracting, Inc.
 Engineer: GSWW, Inc.

Task		Summary		Split	
Task Progress		Rolled Up Task		External Tasks	
Critical Task		Rolled Up Critical Task		Project Summary	
Critical Task Progress		Rolled Up Milestone		Group By Summary	
Milestone		Rolled Up Progress		Deadline	
